

Lockeridge Projects

<http://>

Project manager	
Project dates	20 Jan. 2025 - 28 Jun. 2025
Completion	0%
Tasks	46
Resources	0


## Tasks

Name	Begin date	End date
Payment Milestones	31/1/25	16/6/25
Sign Contracts - 5% Deposit	31/1/25	31/1/25
20% Completion of Excavation	2/4/25	2/4/25
40% Completion of Pool Shell	21/4/25	21/4/25
20% Completion of Pool Tiling	17/6/25	17/6/25
10% Equipment Install	4/6/25	4/6/25
5% Final Payment	5/6/25	5/6/25
Steel Shed	3/2/25	6/2/25
Remove contents of shed	3/2/25	4/2/25
Dismantle shed	5/2/25	5/2/25
Clear driveway obstructions	6/2/25	6/2/25
New west-side lean-to	20/1/25	23/1/25
clear of all obstructions	20/1/25	20/1/25
framing	21/1/25	21/1/25
gutters & drainage	22/1/25	22/1/25
polycarbonate roof sheeting	23/1/25	23/1/25
Loggia	7/2/25	12/2/25
Dismantle existing loggia	7/2/25	11/2/25
Remove artificial turf sheet	12/2/25	12/2/25
Building Permit Application	3/2/25	28/3/25
Building Permit Issued	31/3/25	31/3/25
Pool construction	31/3/25	16/6/25
Excavation	31/3/25	1/4/25
Formwork	2/4/25	7/4/25
Reinforcing	8/4/25	10/4/25
Plumbing rough-in	11/4/25	14/4/25
Electrical rough-in	15/4/25	16/4/25
Pour pool shell	17/4/25	18/4/25
Pour paving/deck slab	17/4/25	18/4/25
cure shell	21/4/25	29/5/25
waterproofing	30/5/25	30/5/25
plumbing fit-off	2/6/25	2/6/25
tiling	3/6/25	16/6/25
equipment install/fit-off	3/6/25	3/6/25
commissioning	4/6/25	4/6/25
Re-build Loggia	26/5/25	2/6/25
Carpentry	26/5/25	29/5/25
Roofing	30/5/25	2/6/25

Tasks

Name	Begin date	End date
Pool fencing	26/6/25	27/6/25
spigots	26/6/25	26/6/25
main fence	27/6/25	27/6/25
gate	27/6/25	27/6/25
Hard landscape	1/5/25	11/6/25
Decking	3/6/25	11/6/25
Garden bed wall	1/5/25	5/5/25
Paving	6/5/25	8/5/25

Gantt Chart

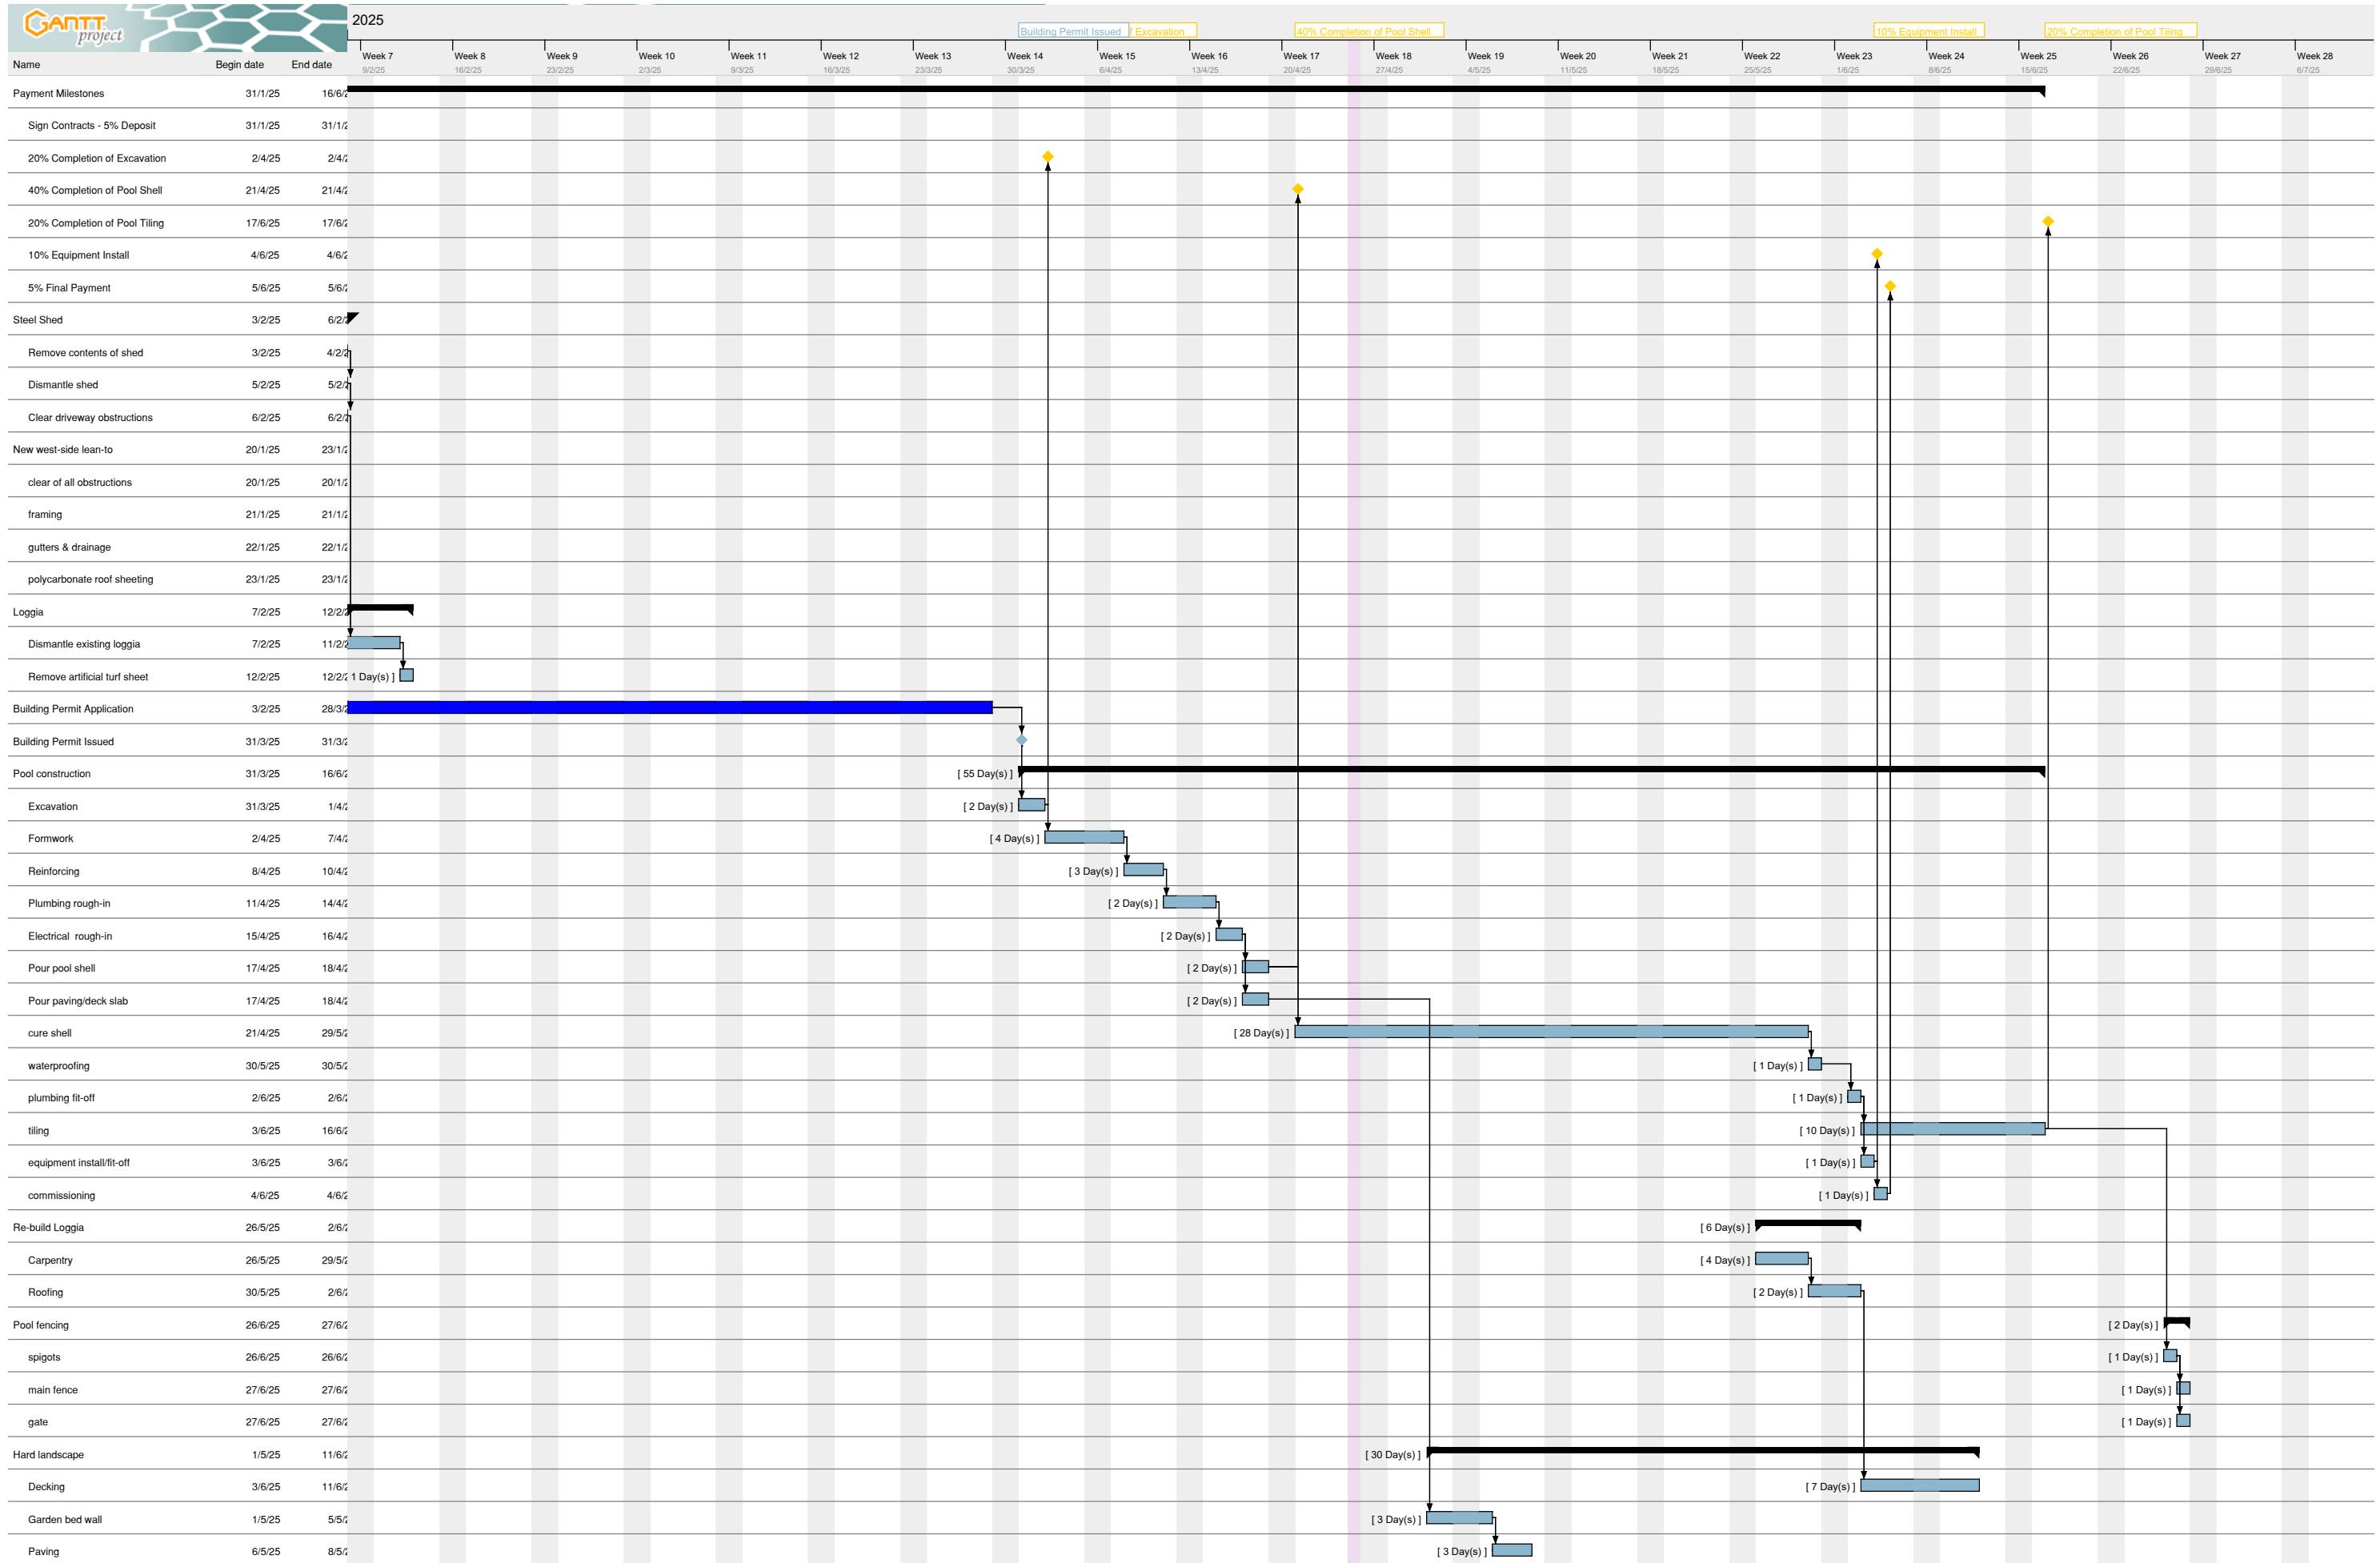

## Resources Chart

